



Berkmar/Central Gwinnett Relief Cluster High School

February 11, 2015

Table of Contents

Berkmar/Central Gwinnett Relief Cluster High School

SECTION 1	PROGRESS SUMMARY
SECTION 2	PROJECT PHOTOS
SECTION 3	PROJECT SCHEDULE
SECTION 4	SUBMITTAL & RFI LOGS

Section 1

PROGRESS SUMMARY

BCG Progress Summary – 2/11/2015

Work Completed or In Progress This Period (Through February 11, 2015):

General

- Site Cleanup Continuing
- EIFS—Complete

Curtainwall

- Gym Glass and Glazing Started
- Mainstreet Vestibule Glass and Glazing Started

Roofing

- West Gym Canopy Metal Roof Complete
- West Gym Canopy Soffits - 90%
- East Gym Canopy Metal Roof and Soffits - 50%

Concessions / Stadium / Pressbox

- Final Paint Complete
- Ticket Booth Coiling Shutters Installed
- Awaiting Architectural Punch

Project Sequences on South Half of Building:

Location/Task: [Sequences 1, 2, 12, & 14](#) (Area between CL's 6-12 & A-F on both floors)

- Architect Punch List Generated for Partial of Sequences 1 and 2
- Final Cleaning - 85%
- Punch Started in Sequence 1
- Ceramic Tile Caulk Joints in sequences 1 and 2 - 90%
- Fire extinguishers placed in cabinets
- Note that Frazier Services is still working above ceilings throughout



Location/Task: [Sequences 4, 5, 15, & 16](#) (Area from CL 6-12 from K-Q on both floors)

- Punch list preparations
- Final Cleaning - 90%
- Awaiting Architectural Punch



BCG Progress Summary – 2/11/2015

Location/Task: [Sequences 6 & 7 - \(Area from CL 1-6 from A-E\)](#)

- Choral Stage Handrails - Installed
- Choral Room Acoustical Panels Installed
- Band Room Acoustical Panels Underway
- Carpet and VCT Complete
- Fire extinguishers Installed
- Wood Doors Underway



Location/Task: [Sequence Eight](#)

- Ceiling Tile - Complete
- Auditorium Wood Paneling - Underway
- Auditorium Acoustical Panels Underway
- Auditorium Seating Layout Complete
- Auditorium Floor Staining Complete
- Auditorium Wood Floor System Started
- Auditorium Handrails Underway



Location/Task: [Sequence Nine Kitchen & Café](#)

- Kitchen Tile Epoxy Grout - Complete
- Kitchen Equipment Installation Underway
- Café Pendant Light Fixtures Complete
- Commons Area Sconce Lighting - 99%

Location/Task: [Sequence Ten \(Aux Gym & Support Rooms\)](#)

- Wood Floor System Started
- Awaiting Engineer OH Punch

Location/Task: [Main Gym Addition \(Sequence 11\)](#)

- Blockfill Paint - 90%
- 1st Coat Paint - 85%
- Gang Bath Floor Tile - Complete
- Toilet Fixtures Complete
- Curtainwall Glass and Glazing Started
- Ticket Booth Coiling Shutter Installed
- Wood Flooring Started



Location/Task: [Main Street](#)

- Ceramic Tile Continuing

BCG Progress Summary – 2/11/2015

BCG Expected Through 3-11-15

Field House

- Exterior Punch Starting

Concessions / Stadium / Pressbox

- Punch Work Starting
- C.O. Issued for Concessions, Pressbox, and Ticket Booths

General Sitework

- Asphalt Topping Complete

Shell and Canopies

- Canopy Metal Trims, Soffits, Gutters, Downspouts - Completing
- Curtainwall Continuing

Sequences (Next 30 Days)

Location/Task: [Sequence 1, 2, 12, & 14](#) (Area between CL's 6-12 & A-E on both floors)

- Architectural Punchlist Corrections - Complete (Depending upon when the punchlists are received)



Location/Task: [Sequences 4, 5, 15 & 16](#) (Area from CL 6-12 from K-Q on both floors)

- Architectural Punchlists Generated
- Punchlist Corrections - Underway



BCG Progress Summary – 2/11/2015

Location/Task: [Sequences 6 & 7- \(Area from CL 1-6 from A-E\)](#)

- Final Painting Complete on Corridors
- TV Studio Pipe Grid Complete
- Wood Doors Complete
- Architectural Punch Generated



Location/Task: [Sequence Eight](#)

- Stage Wood Floor Complete
- Woodwork Complete
- Wood Doors Complete
- Acoustical Panels Complete



Location/Task: [Sequence Nine Kitchen and Café](#)

- Kitchen Equipment - Complete
- Acoustical Panels Underway
- Ceramic Tile Continuing



Location/Task: [Sequence Ten \(Aux Gym\)](#)

- Wood Flooring - Continuing
- Telescoping Bleachers - Started



BCG Progress Summary – 2/11/2015

Location/Task: Main Gym Addition (Sequence 11)

- Curtainwall Glass and Glazing - Completing
- Tile Floors Continuing
- Toilet Partitions Continuing
- Final Painting Continuing
- Wood Flooring Continuing



Location/Task: Main Street

- Final Painting Continuing
- Ceramic Tile Continuing
- Acoustical Panels Continuing



BCG Progress Summary – 2/11/2015

Significant Materials Received This Period:

- Telescoping Bleachers

Significant Decisions / Actions / Meetings

- Contract Executed March 28, 2013
- Notice to Proceed issued on April 1, 2013
- Phase I Erosion Control Completed May 2, 2013
- Pre-Concrete/Masonry Meeting held April 30, 2013
- Pre-Roofing Meeting held May 20, 2013
- Unforeseen Site Condition Encountered - Significant Rock Encountered Beneath Slab on May 1, 2013. Underground plumbing cannot be installed.
- Pre-Blast Meeting held May 28, 2013
- Interior Test Blast Performed on May 31, 2013
- Interior Blasting Started on June 10, 2013 (Underground Plumbing cannot install until blasting is complete in first few Sequences)
- First Slab Pour was made on July 17, 2013.
- Repairs needed throughout building to existing roof connections. Time delay is unknown but this scope is extensive and must be identified and repaired prior to fireproofing application. 1st section identified on 10-7-13.
- Metal Lath is now required over the existing roof decking as it cannot be verified to be UL rated. Time and cost are both impacted. As of 11-20-13 the change request has not been approved. We have released the work to keep the project going.
- A directional rock bore is needed to get the acid waste line out of the building along the north wall. This will require air tracking to identify rock, blasting of rock, excavation of a pit to sit the boring rig at elevation, then boring under north foundation through rock. This has impacted schedule. (Update—This was completed the week of February 3rd.)
- Second floor of gym was poured on July 25, 2014.
- Junior Achievement Program and CIET Program started in December of 2014.
- Field House TCO acquired January 2, 2015 . Principal and approximately 12 other staff members occupied the building.
- The first architectural punchlist was generated on February 4, 2015.

BCG Progress Summary – 2/11/2015

Change Orders Executed: Five

- CO #1 dated March 6, 2014. Includes site allowances as well as CR #'s - 22, 36, 33, 25, 7, 39.
- CO #2 dated March 8, 2014. Includes CR#'s - 1, 2, 3, 4, 5, 6, 9, 10, 12, 14, 18, 19, 20, 21, 24, 26, 27, 28, 29, 30, 34, 35, 38, 40, 50.
- CO #03 dated July 10, 2014. Includes CR #31.
- CO #04 dated August 19, 2014. Includes CR#'s - 41, 42, 43, 44, 45, 46, 51, 52, 53, 55, 56, 57, 59, 60, 61, 62, 63, 64, 65, 66
- CO #05 dated November 17, 2014. Includes CR #'s - 92 and 93.

Change Order Request/Proposal Status:

- CR#01 - French Drains \$2,822.00
- CR#02 - Crush existing Slabs - \$0.00
- CR#03 - Existing Metal Decking Oxidation Repairs - \$1,638.00
- CR#04 - Replace Damaged Existing Metal Decking - \$31,760.00
- CR#05 - Alternate Stair Manufacturer Credit - <\$20,000.00>
- CR#06 - French Drains at Storm Line A - \$3,053.00
- CR#07 - Track Mounted Breaker in July 2013 - \$8,062.50
- CR#08 - Additional Threaded Couplers - VOID
- CR#09 - Outlet Control Structure Trash Rack - \$4,837.50
- CR#10 - Metal Decking to Infill Existing Roof Openings - \$1,999.50
- CR#11 - VOID
- CR#12 - ASI 01 - <\$376,544.00>
- CR#13 - Second Floor Toilet Carriers - VOID
- CR#14 - Metal Lath for Spray Fireproofing - \$172,260.00
- CR#15 - Testing for Drilled Pier Locations - \$2,649.96 - Void
- CR#16 - ASI 2 & 3 - VOID
- CR#17 - Drilled Pier Redesign - \$109,342.34 - VOID
- CR#18 - Replace Section of Existing Slab that was Damaged from Required Blasting - \$36,831.99
- CR#19 - Rock Drilling for North Site Light Pole Bases - \$11,026.97
- CR#20 - GFCI Outlets per RFI #66 - \$2,785.33
- CR#21 - Sanitary Pipe Elevation Adjustment (N Side Building) - \$3,655.00
- CR#22 - Track Mounted Rock Hammer for October - \$35,475.00
- CR#23 - Structural Shoring Rental over existing Transformer - \$2,634.83 - VOID
- CR#24 - Sanitary Sewer Outside Drops - \$7,929.20
- CR#25 - Track Mounted Breaker for November 2013 - \$35,475.00
- CR#26 - Water Line Revisions - \$122,467.00
- CR#27 - Stop Irrigation Line Short - <\$2,130.00>
- CR#28 - Additional Condensate Drain Hubs - \$6,569.33
- CR#29 ASI #4 - \$23,650.45
- CR#30 ASI #5 - \$8,439.00
- CR# 31 ASI #6 - \$587,598.00 CO#3
- CR#32 - Replace remainder of fire line \$73,769.15—VOID
- CR#33 - Interior Blasting
- CR#34 - Roof Asphalt Credit <\$20,550.00>
- CR#35 - Structural Angle from RFI 37. \$2,074.75

Continued on next page...

BCG Progress Summary – 2/11/2015

- CR#36 - Track Hammer Aug –Sept 2013 \$61,812.50
- CR#37 - Void
- CR#38 - Repairs to existing structure 1 - \$18,499.25
- CR#39 - Change Order No 1 Proposal - VOID
- CR#40 - Media Center Radius Wall Parapet - \$3,052.53
- CR#41 - Locker Panel to Gypsum - <\$47,090.37>
- CR#42 - Repairs to existing structure 2 - \$39,898.71
- CR#43 - Replace two 2.5K3 Joists at Elevator \$483.75
- CR#44 - Revisions to second floor door hardware \$1,444.80
- CR#45 - Joist Bearing at Concessions - \$6,342.50
- CR#46 - Rock Bore at Acid Waste Line \$63,968.34
- **CR#47 - Interior Rock Excavation for Plumbing and Electrical \$168,787.00**
- CR#48 - VOID
- CR#49 - VOID
- CR#50 - Reinforcing for Drilled Piers \$23,558.00
- CR#51 - Repairs to existing structure 3 - \$53,468.80
- CR#52 - Power to circulating pump in janitor closet - \$4,056.67
- CR#53 - Existing joist correction - \$2,580.00
- CR#54 - Data Room Changes - \$60,805.85 - **VOID**
- CR#55 - Site Rock - \$21,476.32
- CR#56 - Blasting for South Canopy Footings - \$43,550.08
- CR#57 - Hood Changes - \$3,505.58
- **CR#58 - Relocation of water lines through future JA space - \$2,614.40**
- CR#59 - Drilled Pier Concrete Credit <\$6,000.00>
- CR#60 - Grinnell Coupling Credit - <\$14,422.00>
- CR#61 - Ernst Concrete Credit - <\$17,190.00>
- CR#62 - Auditorium Stage Vapor Barrier Credit - <\$450.00>
- CR#63 - Site Rock removal from South Elevation blasting Part 2- \$24,639.00
- CR#64 - Power to fan coil and condensing unit in Data Room - \$3,530.30
- CR#65 - Duct Grilles in Room 1.2.025 - \$2,185.48
- CR#66 - Power to drinking fountains on main street - \$1,597.45
- CR#67 - Railing on Ramp at Stadium - \$28,926.40
- CR#68 - Floor Leveling - \$56,593.60
- CR#69 - Fire Alarm Proposed VE - <\$17,910.00>
- CR#70 - Pressure Drill Light Pole Bases - \$6,884.33
- CR#71 - Irrigation June, July & Aug 2014 - \$962.23
- CR#72 - Valves at Boilers - \$4,770.75
- CR#73 - Irrigation for Sept 2014 - \$12,148.51
- CR#74 - Power to Hoist on House Lighting - \$2,732.03
- CR#75 - Multipurpose Lighting Change - \$5,936.04
- CR#76 - Drain Pans over Electrical Room 1.1.081 - \$1,485.37
- CR#77 - Cable System for Smoke Hatch Pulls - \$13,271.72
- CR#78 - Provide Power to Door Operator at South Entrance - \$959.14

Continued on next page...

BCG Progress Summary – 2/11/2015

- CR#79 - Relocate 2 Receptacles in Room 1.034 for Casework - \$386.26
- CR#80 - Flange Kits on Lay In Fixtures beneath Balcony - \$693.32
- CR#81 - Power to Motorized Shutter at Dish Return - \$898.38
- CR#82 - Second Sink in Art Room 1.1.419 - \$2,063.67
- CR#83 - Asphalt Paving on South Drive - \$37,508.36
- CR#84 - Floor Prep for VCT on North Existing Slab - \$12,127.59
- CR# 85- HVAC Boiler lines crossed per RFI #203 - \$13,388.90
- CR# 86- VOID Multipurpose Valves for Boilers - DUPLICATE ENTRY
- CR# 87 - Field House Mechanical Systems - \$44,651.01
- CR# 88 - Pipe Bollards at Trash Compactor - \$1,453.90
- CR# 89 - Attendance Fire Shutter - \$7,030.80
- CR# 90 - Repair Conductors at Baseball Field - \$10,573.79
- CR# 91 - Power to Concessions Sprinkler Pump - \$666.19
- CR# 92 - Junior Achievement
- CR# 93 - CIET
- CR# 94 - Stair 5 Ductwork - \$2,109.24
- CR# 95 - Masonry Chases -
- CR# 96 - Data Room Revisions Revised - \$8,307.50
- CR# 97 - Field House Fire Hydrant - \$6,238.75
- CR# 98 - Credit on Softball and Baseball Backstops <\$9,000.00>
- CR# 99 - Install a P-7H Work Room Sink in Work Room 1.2.117—\$1,526.60
- CR# 100 - Floor Box in Media Center \$618.45
- CR# 101 - Mainstreet Beam Box Outs - \$5,581.24
- CR# 102 - Wood Floor Sealer—\$13,863.05
- CR# 103 - Tennis Court Unsuitable Soil Remediation - \$4,939.52
- CR# 104 - Storm Line Relocation for Jack and Bore - \$4,959.22
- CR#105 - Final Power Bill Invoice—\$586.33
- CR# - Frazier Controls Credit <\$47,000>
- CR# - HVAC Insulation Credit
- CR# - HVAC Shop Drawing Credit
- CR# - Pole Vault, Shot Put, Discus, Toeboards
- CR# - C Channel at West Gym Elevation for Curtainwall
- CR# - November 2014 Rock Removal from West Canopy and Main Entrance

Section 2

PROJECT PHOTOS

Project Photos



Berkmar/Central Gwinnett Relief Cluster High School 2/01/15



Berkmar/Central Gwinnett Relief Cluster High School 2/01/15

Project Photos





Berkmar/Central Gwinnett Relief Cluster High School 2/01/15

Section 3


PROJECT SCHEDULE

Berkmar High School - Project Schedule Look Ahead

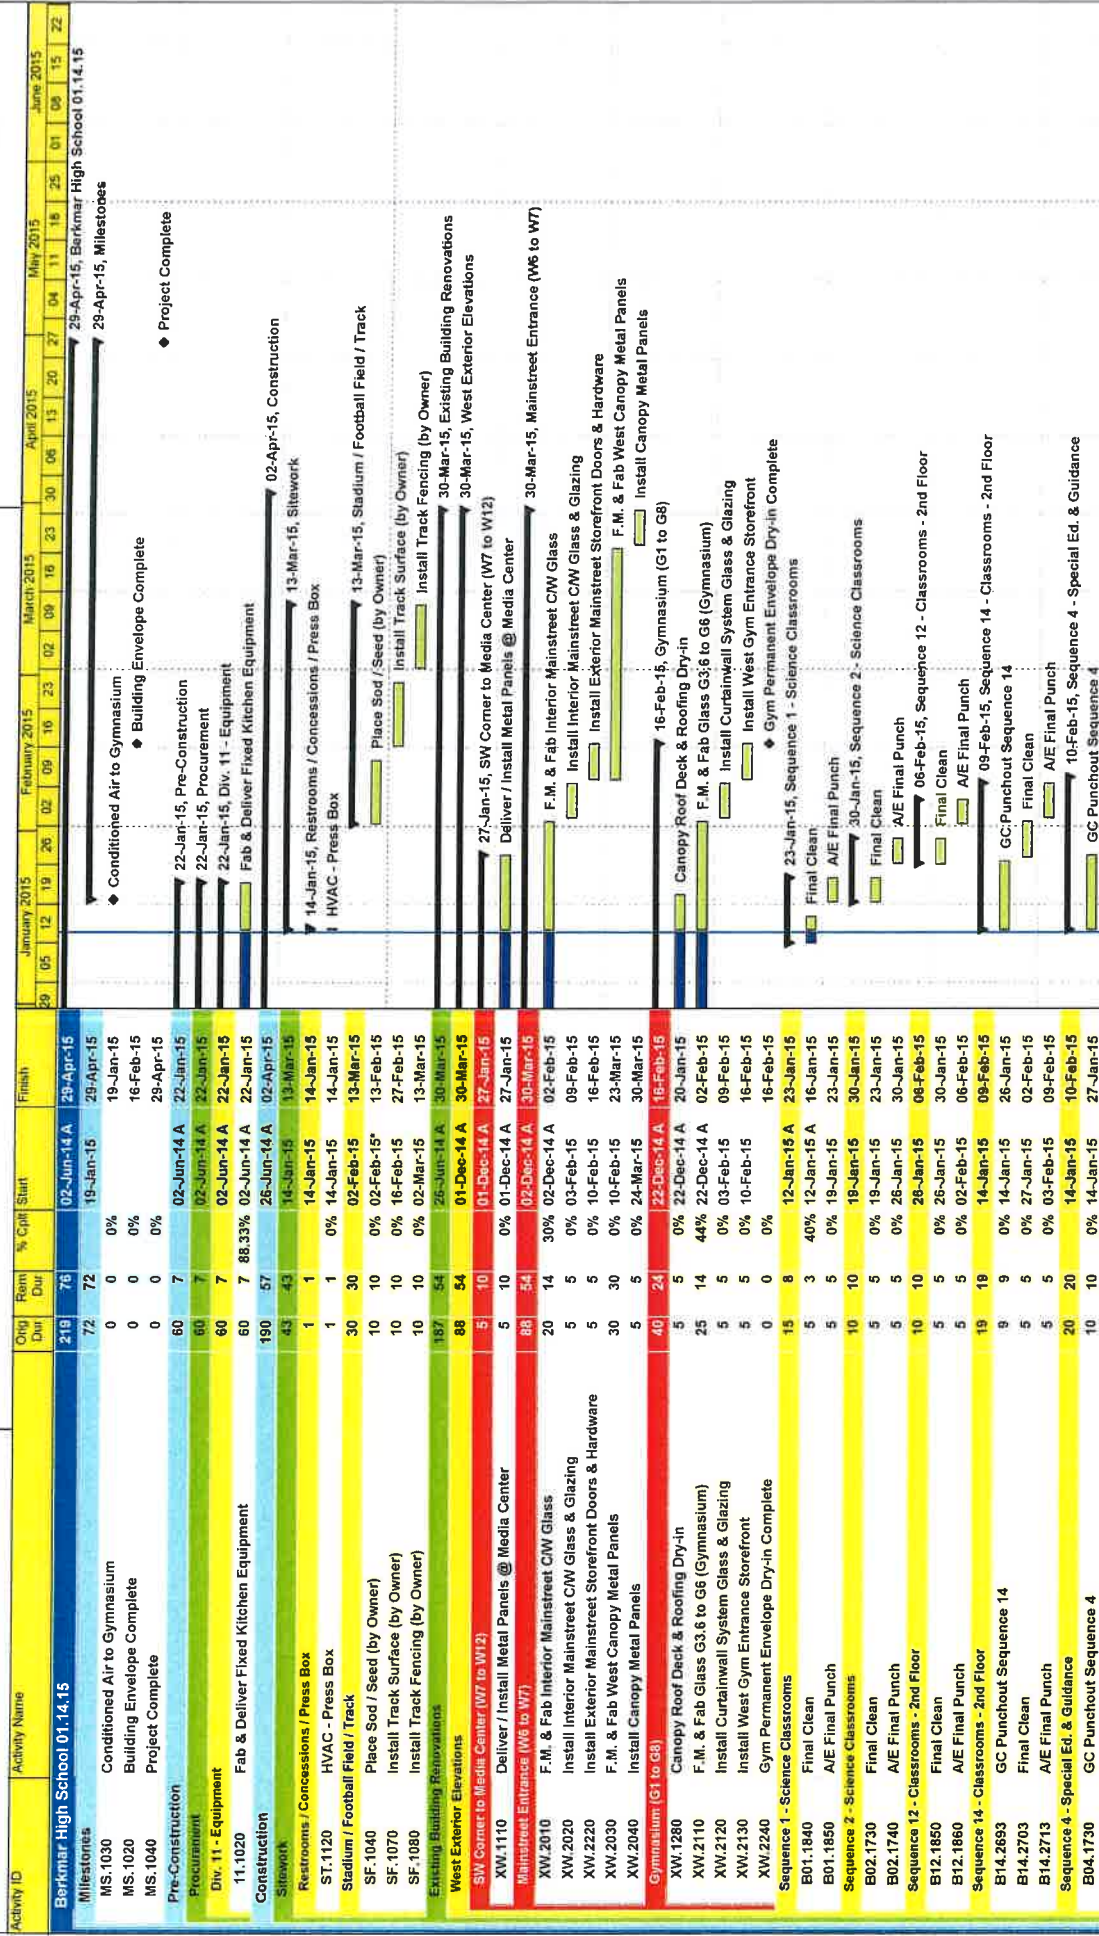


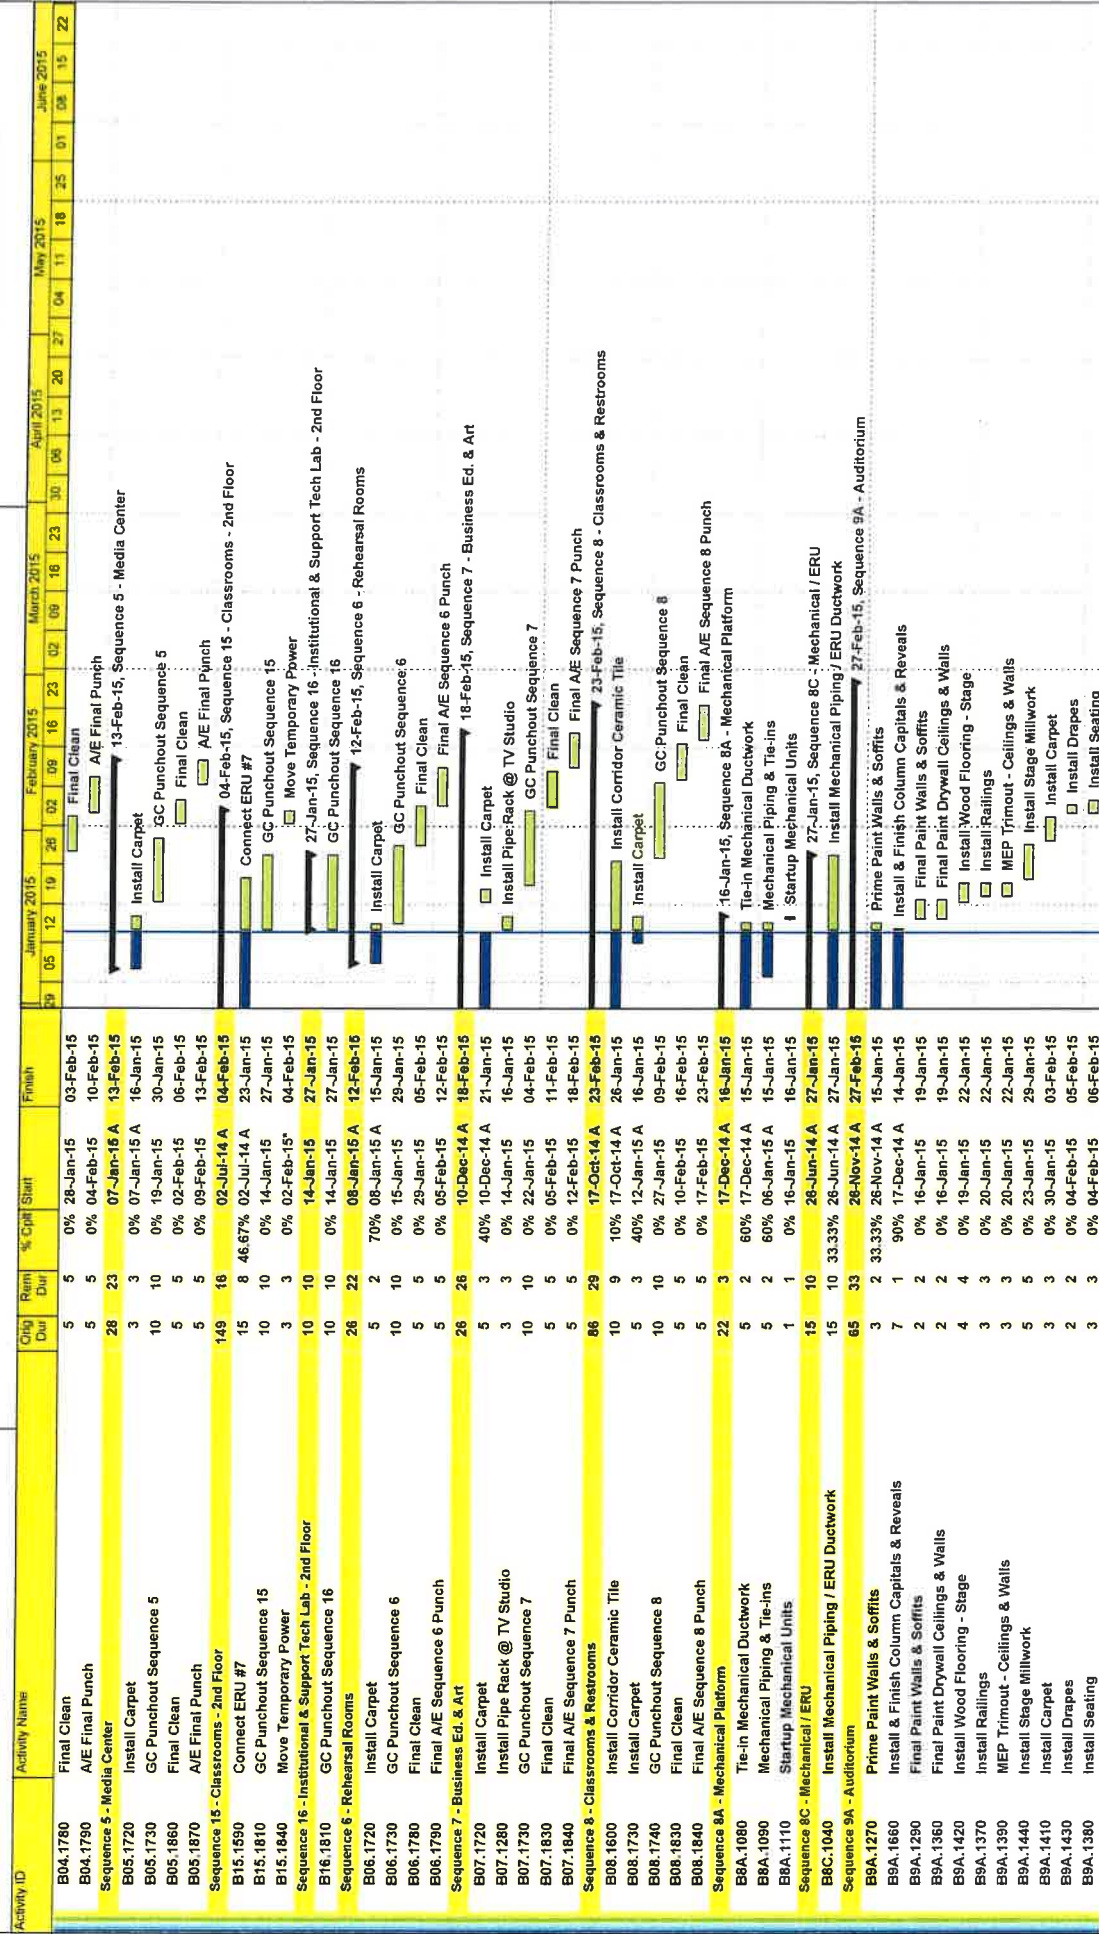

Berkmar High School - Project Schedule Look Ahead

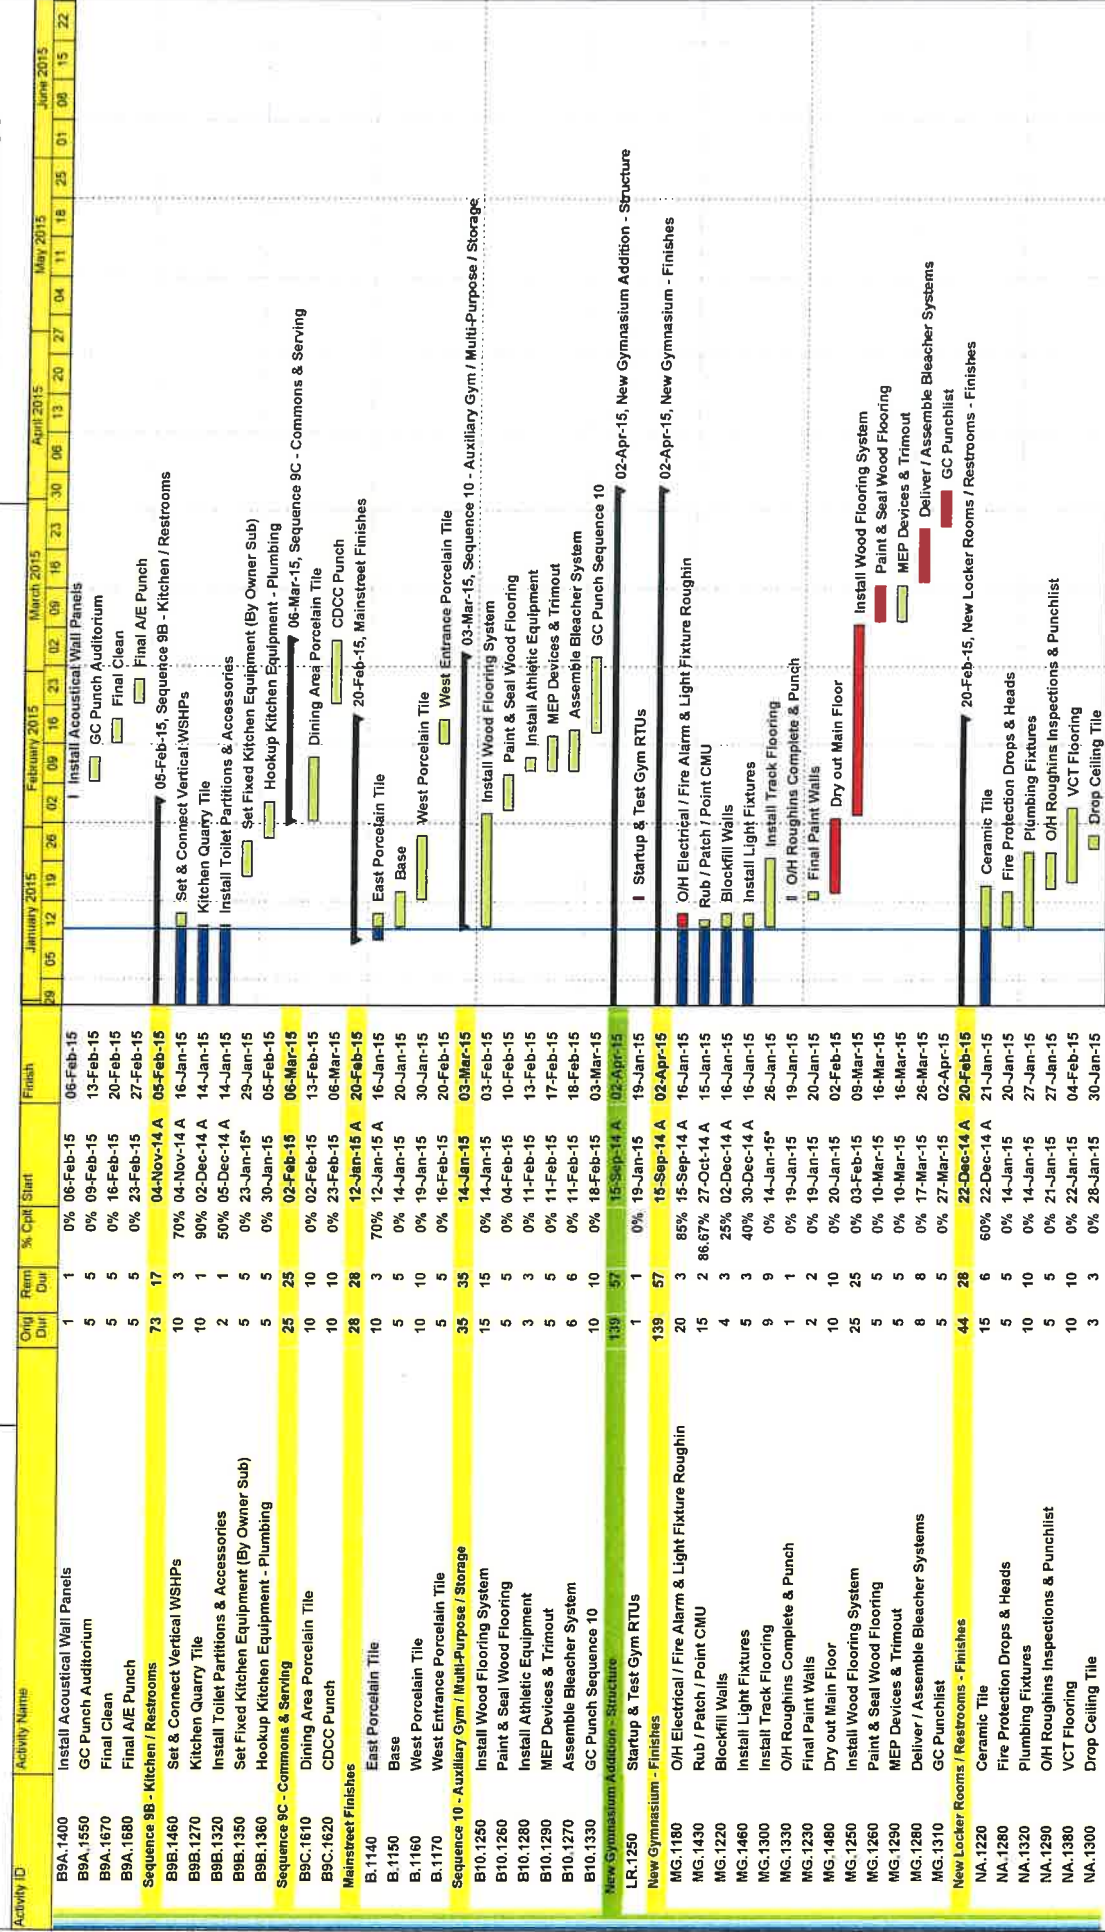

Berkmar High School - Project Schedule Look Ahead

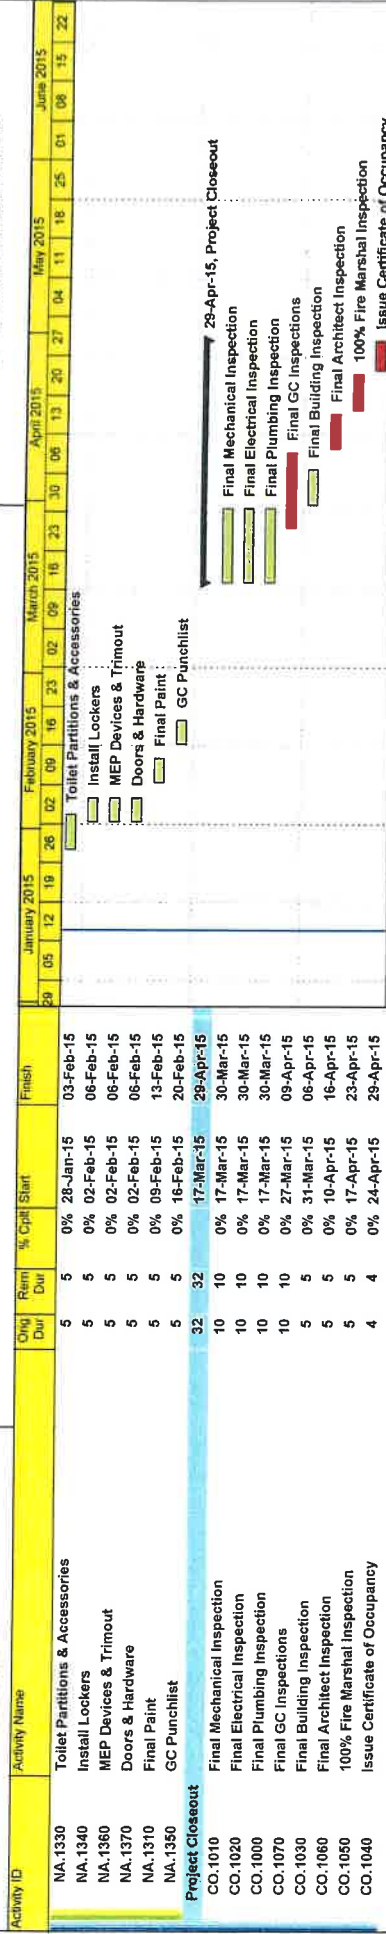

Section 4

SUBMITTAL & RFI LOG

RFI REPORT - ALL

PROJECT: Berkmar/Central Gwinnett Relief Cluster High School
 MANAGER: Henry Irvin
 PREPARED BY: Bryan Burnette
 DATE: 2/11/2015



ID	Subject	Status	Sent	Closed
00001	Roofing Asphalt	Closed	3/28/2013	4/12/2013
00002	RFI - Hollow Core Elevated Slabs	Closed	4/12/2013	4/17/2013
00003	RFI - Sewer Piping	Closed	4/12/2013	4/25/2013
00004	RFI - Hollow Core Bearing Condition	Closed	4/17/2013	4/25/2013
00005	RFI 5 - Electrical Switchboard and Transformer Location	Closed	4/17/2013	6/6/2013
00006	RFI # 6 - Hollow Core Bearing Angle Welding Options	Closed	4/26/2013	4/30/2013
00007	RFI # 7 - Prefabricated Metal Stair System	Closed	5/9/2013	5/13/2013
00008	RFI # 8 - Column Ties	Closed	5/9/2013	7/3/2013
00009	RFI 09 - Hollow Core Design Loads	Closed	5/9/2013	5/14/2013
00010	RFI 10	Closed	5/9/2013	5/13/2013
00011	RFI 11 - Load Bearing Demolition	Closed	5/9/2013	5/23/2013
00012	RFI 12	Closed	5/10/2013	7/3/2013
00013	Metal Stairs	Closed	5/22/2013	5/23/2013
00014	RFI #14 - Metal Stair Loads and Support	Closed	5/28/2013	7/3/2013
00015	RFI # 15 - Concrete Placement	Closed	5/29/2013	6/6/2013
00016	RFI - Atlanta Structural Precast	Closed	6/3/2013	6/20/2013
00017	Top of CIP Walls Between Grids SC and SE	Closed	6/3/2013	6/18/2013
00018	Precast Raker Bearing Elevations on CIP Pedestals (LEAP RFI-05)	Closed	6/3/2013	6/27/2013
00019	CIP and Precast End Walls Grid SC to SD (LEAP RFI-06)	Closed	6/3/2013	6/27/2013
00020	Top of Scoring Level Spandrel Elevation (LEAP RFI-07)	Closed	6/4/2013	6/20/2013
00021	Insufficient Tolerance Precast to Precast and Precast to CIP (LEAP RFI-08)	Closed	6/4/2013	6/18/2013
00022	Concessions Level Stair Opening (LEAP RFI-09)	Closed	6/5/2013	6/20/2013
00023	Top of Precast Wall Behind Concessions Level Stairs (LEAP RFI-11)	Closed	6/4/2013	6/20/2013
00024	MEP Trade Coordination (LEAP RFI-12)	Closed	6/6/2013	9/20/2013
00025	Precast Aisle Steps (LEAP RFI-10)	Closed	6/6/2013	6/18/2013
00026	RFI 26 - Trench Rock Width	Closed	6/17/2013	6/18/2013
00027	Exterior CMU at Two-Story Admin Area on South Wall	Closed	6/20/2013	7/2/2013
00028	Electrical Fixture Mounting Heights	Closed	6/27/2013	8/29/2013
00029	Structural Clarifications	Closed	6/28/2013	7/2/2013
00030	Stair Nosing Thickness & HVAC Equipment Size at Press Box Roof for Handrail Fabrication	Closed	7/3/2013	8/12/2013
00031	Specified Pipe Size for Handrails	Closed	7/11/2013	7/18/2013
00032	RFI # 32 - Beam Bearing Condition	Closed	7/19/2013	7/25/2013

ID	Subject	Status	Sent	Closed
00033	Old Norcross Sidewalk	Closed	7/24/2013	9/30/2013
00034	Angle Detail	Closed	7/30/2013	8/5/2013
00035	RFI 17	Closed	6/17/2013	7/30/2013
00036	Offset Beam Connection	Closed	8/2/2013	8/5/2013
00037	Potential Beam Needed for HVAC Duct	Closed	8/6/2013	8/15/2013
00038	Clarification to RFI # 37 Response	Closed	8/8/2013	9/30/2013
00039	Toilet 1.1.091	Closed	8/8/2013	8/12/2013
00040	Clash in Footing and Main Trunk Line at Concessions	Closed	8/12/2013	8/15/2013
00041	Ductwork Clash with Steel Beam Plate	Closed	8/15/2013	8/29/2013
00042	Wall Hung Toilets	Closed	8/15/2013	8/29/2013
00043	Misc Questions	Closed	8/20/2013	9/20/2013
00044	Handicapped Seating For Gymnasium - Dimensions	Closed	8/23/2013	8/29/2013
00045	Elevations for "A" Linec	Closed	8/27/2013	8/29/2013
00046	Emergency Generator Gas Line	Closed	9/4/2013	9/4/2013
00047	Brick Lintel Bearing Condition	Closed	9/6/2013	9/9/2013
00048	Rock Bearing Footings Clarification	Closed	9/6/2013	9/20/2013
00049	Field House Beam Bearing Condition	Closed	9/6/2013	9/9/2013
00050	Storm Line Demo	Closed	9/6/2013	9/9/2013
00051	Columns in Storefront Openings	Closed	9/6/2013	9/20/2013
00052	Beam Elevation Clarification - CDCC Sequence 4	Closed	9/11/2013	9/12/2013
00053	Duct relocation - M2-25	Closed	9/12/2013	9/25/2013
00054	Drilled Pier Exploratory Drilling Results	Closed	9/12/2013	10/17/2013
00055	Connection from Site Stair Walls to Field House Wall	Closed	9/12/2013	9/12/2013
00056	Retaining Wall on South East Corner	Closed	9/16/2013	9/17/2013
00057	Clarification on column locations/spacing	Closed	9/16/2013	9/17/2013
00058	Splice Detail For Drilled Pier Reinforcing Steel	Closed	9/17/2013	9/19/2013
00059	Anchor Bolt Field Dimensions at Field House	Closed	9/18/2013	10/15/2013
00060	Load Bearing Wall Request	Closed	9/23/2013	9/24/2013
00061	Hollow core Dimension Clarification	Closed	9/24/2013	10/8/2013
00062	Elevation Clarification SQ 5	Closed	9/26/2013	9/30/2013
00063	Duct Sizing	Closed	10/4/2013	10/7/2013
00064	Decking Spacing at Stadium	Closed	10/10/2013	10/15/2013
00065	Steel Elevation Clarification in SQ 3	Closed	10/17/2013	10/17/2013
00066	Misc. Electrical Details	Closed	10/17/2013	10/18/2013
00067	Plumbing Invert Elevation	Closed	10/21/2013	10/21/2013
00068	Chilled Water Line	Closed	10/21/2013	10/31/2013
00069	Beam at Stair #8	Closed	10/22/2013	10/30/2013
00070	Field Splice at Auditorium Trusses	Closed	10/23/2013	11/18/2013
00071	Brick Bottom Band Condition at Corners	Closed	10/24/2013	10/25/2013
00072	Curb at East Side of Building	Closed	10/24/2013	11/18/2013

ID	Subject	Status	Sent	Closed
00073	Beam Connection at Existing Column	Closed	10/24/2013	10/28/2013
00074	Slab at Custodial Closet 1.1.421	Closed	10/29/2013	10/30/2013
00075	Gas Regulators for Science Rooms	Closed	10/29/2013	12/19/2013
00076	Miscellaneous Mechanical Clarifications	Closed	10/31/2013	11/1/2013
00077	Beam Spacing and Angle Sizes at Stadium Steel	Closed	11/1/2013	11/5/2013
00078	Base plate washers	Closed	11/4/2013	12/23/2013
00079	Tube Steel Column Embed Plates Along WP.7	Closed	11/5/2013	11/5/2013
00080	Spirals for 24" Diameter Drilled Piers	Closed	11/7/2013	11/8/2013
00081	Roof Nailers at North Wall	Closed	11/12/2013	11/15/2013
00082	Roof Condition at Old Administration Area	Closed	11/13/2013	11/15/2013
00083	Joists Spanning over Auditorium	Closed	11/15/2013	11/19/2013
00084	Column at Elevator Pit in the Main Gym	Closed	11/15/2013	11/27/2013
00085	Anchor Bolts Near Commons	Closed	11/18/2013	12/30/2013
00086	Parapet Condition at West Wall	Closed	11/18/2013	11/18/2013
00087	Electrical Rough-In Coordination With Owner	Closed	11/19/2013	12/19/2013
00088	Knock-Out Panel SQ 6	Closed	11/21/2013	11/25/2013
00089	Cold-Formed Diagonal Metal Bracing to Structure	Closed	11/26/2013	11/29/2013
00090	Field Welded Connections at Truss	Closed	11/26/2013	11/27/2013
00091	Work Room 1.2.117 - Sink	Closed	12/4/2013	12/5/2013
00092	VFD Clarification	Closed	12/4/2013	12/5/2013
00093	Sound Attenuators	Closed	12/4/2013	12/12/2013
00094	Reflected Ceiling Plans - Field House & Stadium Locations	Closed	12/5/2013	12/11/2013
00095	Media Center Clarifications	Closed	12/9/2013	12/16/2013
00096	Ceiling Conflict at Stair #13	Closed	12/9/2013	1/7/2014
00097	Bumper Rail at East Entrance	Closed	12/11/2013	12/11/2013
00098	Sanitary Waste Piping Above Electrical Room	Closed	12/11/2013	12/16/2013
00099	Louver Size at Field House	Closed	12/16/2013	12/17/2013
00100	Dimensions and Loads for Joists	Closed	12/16/2013	12/16/2013
00101	Top of Footing Elevation at North Canopy	Closed	12/16/2013	12/16/2013
00102	Rain Leader Piping - West Side Near Media Center	Closed	12/17/2013	12/19/2013
00103	Joist Bearing Condition at North Exterior Wall	Closed	12/19/2013	12/26/2013
00104	FC-1-11 Refrigerant Pipe Routing	Closed	12/19/2013	12/26/2013
00105	Mechanical Room Piping	Closed	12/19/2013	12/26/2013
00106	Vertical WSHPs and HGRH	Closed	12/19/2013	12/26/2013
00107	Rain Leader Piping At West & North Exterior Walls	Closed	12/20/2013	1/2/2014
00108	Bearing Condition at Old Administration Area	Closed	12/20/2013	12/26/2013
00109	Brick Caulk Color at Color Pattern	Closed	12/30/2013	12/30/2013
00110	Ceiling Conditions Near Computer Lab 1.1.224	Closed	12/30/2013	1/2/2014
00111	Stair #5 Steel Supports	Closed	1/2/2014	1/2/2014
00112	Unidentified FCU	Closed	1/2/2014	1/3/2014

ID	Subject	Status	Sent	Closed
00113	Door Conflict Office 4.1.031 at Field House	Closed	1/3/2014	1/3/2014
00114	Miscellaneous Structural Steel Questions - King Steel SQ 10C	Closed	1/3/2014	1/3/2014
00115	Duct Clash M2-12	Closed	1/9/2014	1/21/2014
00116	Fire Damper at Electrical Room on East Side	Closed	1/10/2014	1/21/2014
00117	Manual Damper Adjustment Locations - M1-17	Closed	1/17/2014	2/4/2014
00118	Electrical Rough-In - Mounting Heights for Electronic Scoreboards (Berkmar)	Closed	1/17/2014	1/22/2014
00119	Floor Drain - P1-22A	Closed	1/21/2014	1/22/2014
00120	Type "LL" & "LL1" Light Fixture Mounting Heights	Closed	1/27/2014	1/27/2014
00121	Power Circuit for Water Heater - Room 1.1.309	Closed	1/27/2014	1/28/2014
00122	Control Clarifications	Closed	1/27/2014	2/17/2014
00123	Smoke Partition Top Detail	Closed	1/28/2014	2/17/2014
00124	Damaged Joist Repair	Closed	2/3/2014	2/3/2014
00125	Spoil Pile on East Side of Site	Closed	2/3/2014	3/3/2014
00126	Downspout Piping Near Grease Traps	Closed	2/3/2014	2/17/2014
00127	WSHP Locations	Closed	2/4/2014	3/19/2014
00128	RTU Sequencing	Closed	2/4/2014	2/18/2014
00129	Clarification on Reviewed Kawneer Shop Drawing, Submittal 08810.01	Closed	2/10/2014	2/11/2014
00130	Bond Beam and Tube Steel Above Door Clarification - Aux. Gym	Closed	2/20/2014	2/24/2014
00131	ERU Disconnect Size	Closed	2/26/2014	3/6/2014
00132	Round Pipe Size Clarification at Field House	Closed	2/26/2014	2/27/2014
00133	Plumbing Piping in Chase Walls for Unfinished/Future Staff Toilets	Closed	2/28/2014	3/3/2014
00134	Mechanical Unit Locations Above Auditorium	Closed	2/28/2014	3/3/2014
00135	Joist Spacing at Auditorium	Closed	3/3/2014	3/3/2014
00136	Baseball and Softball Spot Elevations	Closed	3/6/2014	3/14/2014
00137	Exhaust Fan at Main Mechanical Room/Central Plant	Closed	3/7/2014	3/7/2014
00138	South Canopy Footing Elevations	Closed	3/10/2014	3/13/2014
00139	CWS&R Pipe in Sequence 3 - Unfinished Area	Closed	3/12/2014	3/13/2014
00140	Band Rehearsal Hall 1.1.311	Closed	3/17/2014	3/17/2014
00141	Media Equipment Storage 1.1.028 Duct Location	Closed	3/17/2014	3/17/2014
00142	Linear Bar Diffusers	Closed	3/20/2014	3/26/2014
00143	West Canopy Miscellaneous Elevations and Details	Closed	3/21/2014	3/26/2014
00144	Doors 11434C & 11446C - Hardware Location	Closed	3/26/2014	3/27/2014
00145	TT Style Grills	Closed	3/26/2014	3/26/2014
00146	Miscellaneous Ceiling Conditions at Field House	Closed	3/31/2014	3/31/2014
00147	Storm Piping at North Side of Gymnasium to Structure A11	Closed	3/31/2014	3/31/2014
00148	Condensate Drains for Heat Pumps at Field House	Closed	4/2/2014	4/7/2014
00149	In-Line Pumps	Closed	4/2/2014	4/7/2014
00150	Motor Operators - Overhead Doors	Closed	4/3/2014	4/16/2014
00151	ERU Fan Access	Closed	4/3/2014	4/11/2014
00152	Electrical at Backstop	Closed	4/15/2014	4/17/2014

ID	Subject	Status	Sent	Closed
00153	Boiler In-Line Pump Location	Closed	4/18/2014	4/29/2014
00154	8" Bypass at Boilers	Closed	4/18/2014	4/29/2014
00155	Mechanical Room Piping Arrangement	Closed	4/18/2014	4/29/2014
00156	Utility Sleeves at Stadium Track	Closed	4/23/2014	4/29/2014
00157	Fireproofing on Sprinkler Piping	Closed	4/23/2014	6/30/2014
00158	Downspout size at North Elevation	Closed	4/23/2014	4/28/2014
00159	Sidewalk West of Field House	Closed	4/28/2014	4/29/2014
00160	Miscellaneous Steel Connections	Closed	5/1/2014	5/5/2014
00161	Generator Annunciator at Field House	Closed	5/5/2014	5/19/2014
00162	Bolted Connections at Auditorium	Closed	5/7/2014	5/8/2014
00163	Power to FC-1-7	Closed	5/14/2014	5/23/2014
00164	Sound Booth Ceiling Framing Details	Closed	5/14/2014	7/17/2014
00165	Miscellaneous Steel Connections at Canopy and Aux. Gym	Closed	5/19/2014	5/20/2014
00166	Steel column with headed studs at Main Gym	Closed	5/23/2014	5/27/2014
00167	Soffit Heights at Mainstreet Corridor	Closed	5/30/2014	5/30/2014
00168	Light Pole Bases	Closed	6/9/2014	9/19/2014
00169	Duct Grilles Room 1.2.025	Closed	6/13/2014	6/13/2014
00170	Soffit Framing Conflict in Auditorium	Closed	6/17/2014	6/18/2014
00171	Step Lighting in Auditorium	Closed	6/17/2014	6/18/2014
00172	Control Joint Conditions Around Main Gym	Closed	6/20/2014	6/25/2014
00173	Pre-existing Damaged Girder and Joist	Closed	7/8/2014	7/11/2014
00174	FCU-1-13 Drain Re-routing	Closed	7/8/2014	7/15/2014
00175	Fencing North of Stadium Concessions	Closed	7/9/2014	7/10/2014
00176	T Light Fixtures Above Stage in Auditorium	Closed	7/11/2014	7/11/2014
00177	Light Fixtures in Bathrooms at Field House	Closed	7/15/2014	8/1/2014
00178	Power to Water Coolers in Mainstreet Near Office 1.1.420	Closed	7/17/2014	8/1/2014
00179	Flooring Types at Second Level of Main Gym	Closed	7/17/2014	7/22/2014
00180	Exposed Spiral Duct - Hanging Detail	Closed	7/22/2014	7/28/2014
00181	Clarification Note M3-21 at Col. WH-9 & W8	Closed	7/22/2014	7/28/2014
00182	Mechanical Louver Above Entrance of Stadium Press Box	Closed	7/28/2014	8/1/2014
00183	Grills Between Clouds in Auditorium	Closed	7/29/2014	7/29/2014
00184	Smoke Hatch Interior Release Cables	Closed	8/15/2014	8/18/2014
00185	Exposed beams on South Side of Main Street	Closed	8/15/2014	8/18/2014
00186	Power to Water Heater at Stair 1.1.226	Closed	8/18/2014	8/28/2014
00187	Family & Consumer Science Lab 1.1.206 - Residential Range Hood Duct Size	Closed	8/18/2014	8/27/2014
00188	UU Supply Air Diffusers at Stage	Closed	8/27/2014	8/28/2014
00189	Wall Mounted Light Fixtures at Stairs in Main Gymnasium	Closed	8/28/2014	9/10/2014
00190	Corridor 1.1.340 & 1.1.330 Hub Drains	Closed	9/5/2014	9/8/2014
00191	Valve Tag Book in Lieu of Charts	Closed	9/10/2014	9/15/2014
00192	Ceiling in Room 1.1.082A	Closed	9/16/2014	9/16/2014



Discovery High School
February 11, 2015
9:00 A.M.

NAME	COMPANY	PHONE	EMAIL ADDRESS
Henry Invid	CDCC	75363241	hivin@carroldaniel.com
James Chance	CDCC	770-654-9326	UChance@Carroldaniel.com
Bryan Swannick	CDCC	770-561-0661	bburnette@carroldaniel.com
Jay Willette	CDCC	678-936-0037	jayw@carroldaniel.com
Lance Leavitt	G.F.P	770-519-8416	LANCE@GAINESVILLEFIRE.COM
Phil Roberts	Roberts Comm.	770-231-3656	Robertscommercial@gmail.com
Eric Hamilton	ECI	770-324-6875	eric@eci.us
Dan Wengert	CSA Supply	404-379-5735	dwengert@cbasports.us
Ron Sandoz	Hope	678-296-7486	RONSA@bellsouth.net
Chuck Satterfield	S.C.P	706-200-6658	
Scott Head	Best tilt	770-532-0262	BestCeramicTile@Icloud.com
Dennis Fuller	CSH	706-939-0101	dfuller@CHMECHANICAL.NET
Liberty Adams	Tier 1	771-244-4257	ta@glassyade.com
Noises Garcia	fl.	678 988 5943	
Ronnie Tilley		770 314 6114	
JEFF MILLER	SPSAA	4-232-5453	jmillerspsaa.com
Brent Redman		7 513 6602	
